BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	: Executive Engineer Byatarayanapura Division
Project Name	: Package No.03(Package consists of 21 works)
Consultants	: Rudraprasad Consultants
Project Manager /Team Leader	: Karthik Rechan
Project Start Date	: 22-Oct-18
Project End Date	: 22-Oct-19
Project Length in Months	: 12 months

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
1	Earthwork in surface excavation in ordinary soil for leveling and lowering the ground	Cum	6493.58	6493.58	100	24-10-18	10-06-19	229
3	Removing B.S slab of Drain and stacking as per the directions of the Engineer-in-charge of the work .	Sqm	1729.33	1729.33	100	24-10-18	10-06-19	229
4	Removing and refixing stone slabs of drains and pointing in CM (1:3)	Sqm	7225.02	6330.57	88	24-10-18	10-06-19	229
5	Providing granite slabs of selected quality roughly dressed havinf a size of 7.5 cms thick	Sqm	1805.18	1052.20	58	24-10-18	10-06-19	229
6	Providing granite slabs of selected quality roughly dressed havinf a size of 10 cms thick	Sqm	1774.33	1774.33	100	24-10-18	10-06-19	229
7	Earthwork excavation by manual means in ordinary soil involving an average horizontal throw upto 2meters and an average lift upto 1.5 m,	Cum	9966.47	7736.74	78	05-11-18	29-06-19	236
9	Load for disposal of earth shall be payable at Carriage rates (Lead & Lift) by mechanical means including loading and unloading up to 15kms	Cum	19372.14	14931.73	77	24-10-18	09-07-19	258
11	Providing,laying, spreading and compacting crushed stone aggregates of granite/trap/ basalt to wet mix macadam specification	Cum	5773.44	4304.05	75	08-11-18	10-07-19	244
12	Scarifying bituminous course 50mm to 75mm thick along with premix carpet / surface dressing by road roller attached with scarifier without disturbing the base and stacking the debris	Sqm	8449.88	6477.86	77	02-11-18	02-07-19	242
13	Cleaning the existing WBM Road surface including removing of binding materials and other foreign matter with wire brushes	Sqm	16183.50	16183.50	100	12-11-18	13-07-19	243
14	Providing and applying primer coat with SS bitumen emulsion on prepared surface of granular Base such as WBM WMM including clearing of roud surface	Sqm	24705.56	18655.63	76	12-11-18	13-07-19	243
15	Providing and laying bituminous macadam on prepared surface with crushed coarse aggregates	Cum	821.92	821.92	100	12-11-18	13-07-19	243

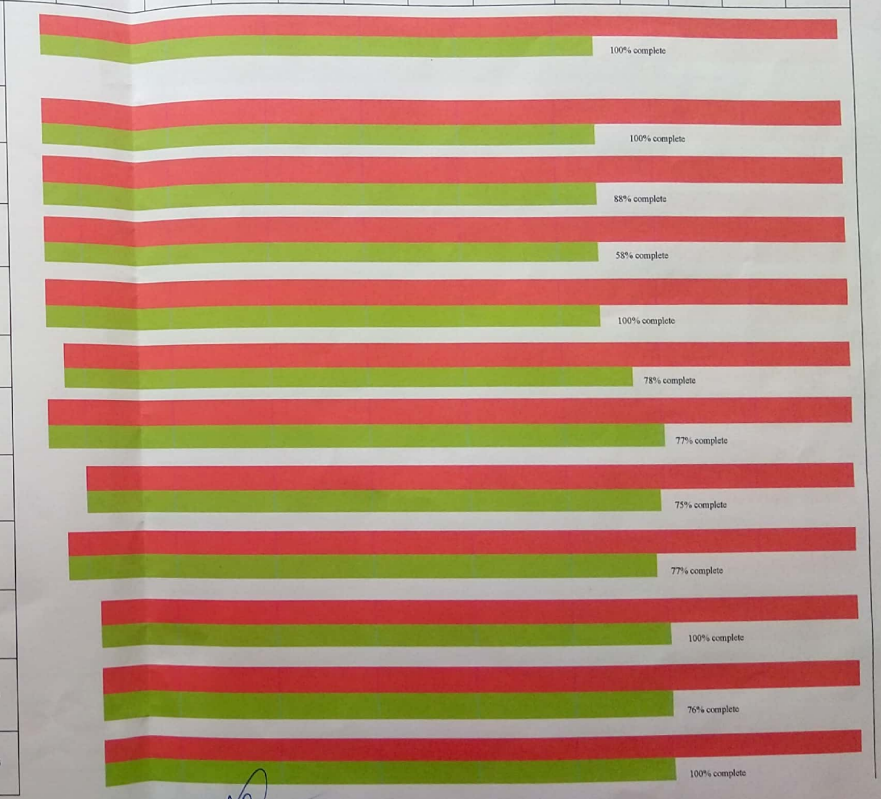

RUDRAPRASAD CONSULTANTS BANGALORE

Assistant Executive Engineer
Vidyaranyapura Sub Division

Scanned with CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	: Executive Engineer Byatarayanapura Division
Project Name	: Package No.03(Package consists of 21 works)
Consultants	: Rudraprasad Consultants
Project Manager /Team Leader	: Karthik Rechan
Project Start Date	: 22-Oct-18
Project End Date	: 22-Oct-19
Project Length in Months	: 12 months

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
17	Cleaning the existing black topped surface with brooms,soft brushes	Sqm	85574.84	81164.94	95	19-11-18	20-07-19	243
18	Providing and applying tack coat using 80/100 grade bitumen (VG10) on prepared black topped surfaces	Sqm	93484.60	83638.07	89	20-11-18	22-07-19	244
19	Providing and laying bituminous concrete 30-40 mm compacted thickness with VG30 Bitumen grade using 40-60 HMP using crushed aggregates	Cum	3938.28	3544.42	90	20-11-18	22-07-19	244
20	Road Marking with Hot Applied Thermoplastic Compound with Reflectrising Glass Beads on Bituminous Surface:- Providing and laying of hot applied thermoplastic compound 2.5 mm thick including reflectorising glass beads	Sqm	3328.88	3140.06	94	24-11-18	25-07-19	243
25	LED Street light.Supply of LED Streetlight with pressure die cast aluminum housing body with optimal heat sink for better thermal dissipation.	No	88.00	88.00	100	20-11-18	18-07-19	240
26	Supplying and Fixing of..... mm dia class A GI pipe bracket up to 2 mtrs long bent at suitable angle and fixing to this bracket 1x40/2x40 watts	No	135.00	135.00	100	20-11-18	18-07-19	240
27	Wiring for lighting/power circuit using one of PVC insulated 1100v grade stranded Aluminium unsheathed wire single	No	440.00	440	100	20-11-18	18-07-19	240
28	Supplying of 1.1 KV LT UG cable having aluminum conductor PVC insulated, extruded	Rmt	150.00	150.00	100	20-11-18	18-07-19	240
29	Labour charges for laying of 1.1 KV class UG cable in existing trench GI pipe / stoneware pipe / on wall / on pole as required.	Rmt	150.00	150.00	100	20-11-18	18-07-19	240
30	Supplying tinned copper lugs and crimping and wiring to terminal point for wire of the following sizes25 sqmm	No	55.00	55.00	100	20-11-18	18-07-19	240

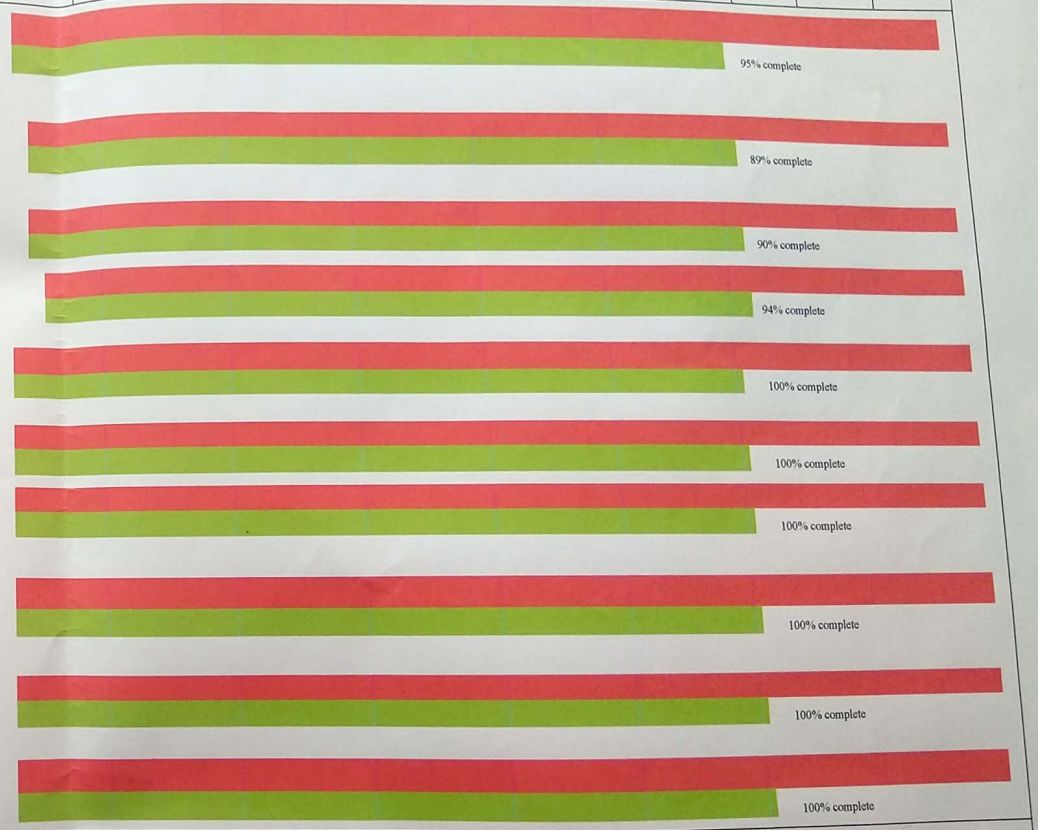

RUDRAPRASAD CONSULTANTS BANGALORE

Assistant Executive Engineer
Vidyaranyapura Sub Division
BBMP, Bangalore - 97

Scanned with CamScanner
